


# Hamilton Avenue Improvements

**District #: 4**  
**Project #: 50171**

**Project Sponsor:** Olema Edwards, Director Parks & Recreation, Debrah Forester Director Bayshore MSTU  
**Fiscal Group:** Parks & Recreation / Bayshore MSTU  
**Project Manager:** Olivier Sureau, PMP  
**Project Scope:** Add boat trailer parking, multi use path, lighting and landscaping

**Design Budget:** \$63,784  
**Construction Budget:** \$3,246,305  
**Architect/Engineer:** RWA  
**General Contractor:** Haskins, Inc.  
**Owner's Representative (CEI):** Johnson Engineering

**Notice to Proceed Date:** 01/10/22 (Haskins)  
**Estimated Substantial Completion Date:** 01/30/23

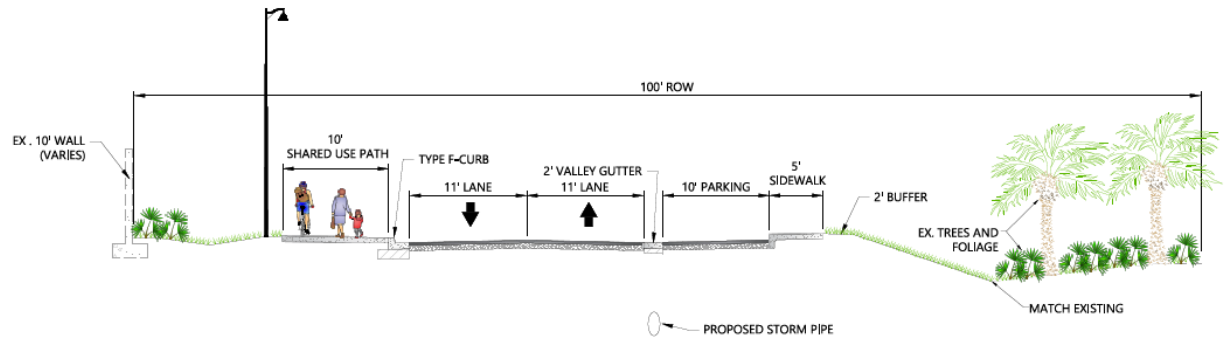

## Milestones/Challenges To Date: 12/20/22

- Construction: Roadway work started on 3/24/22. Walk-thru took place 12/15/22. Punch list in-progress
- CEI: Johnson Engineering: PO & NTP issued. First bi-weekly project progress meeting held on 1/26/22
- City of Naples new watermain in-service. City and County did not enter into an agreement but kept in communication
- Project information sign was placed by pay station at Bayview Park
- Completion of construction expected early 2023

DESCRIPTION OF WORK	% COMPLETE
Design	100%
Permitting	100%
Procurement	100%
Construction	84%
